

London N. Breed Mayor

Mohammed Nuru Director

Ronald Alameida

Acting Deputy Director and City Architect

Building Design & Construction 30 Van Ness Ave., 4th floor San Francisco, CA 94102 tel 415-557-4602

sfpublicworks.org

facebook.com/sfpublicworks twitter.com/sfpublicworks

Quarterly Status Report

October through December 2019



TCFSD – Foundation Piles (November 7, 2019)



TCFSD - Mud Slab (December 17, 2019)



FS 35 – Demolition Complete (October 22, 2019)



FS 31 – Concrete Pad for New Generator

Prepared for the:

- Office of the Chief Medical Examiner
- San Francisco Fire Department
- San Francisco Police Department
- **Public Utilities Commission**

Submitted by Charles Higueras, FAIA Program Manager

Table of Contents

Executive Summary	1
Program Summary and Status	3
Public Safety Building (ESER 2010)	3
Neighborhood Fire Stations (ESER 2010)	5
Neighborhood Fire Stations (ESER 2014)	10
Emergency Firefighting Water System	17
Office of the Chief Medical Examiner (OCME)	18
Traffic Company & Forensic Services Division (ESER 2014)	20
Police Facilities (ESER 2014)	23
Budget, Funding and Expenditures	26
ESER 2010	26
ESER 2014	27
Attachment 1 – Contact Information	29
Attachment 2 – Schedule	30

Executive Summary

The \$412.3 million Earthquake Safety and Emergency Response 2010 (ESER 2010) Bond Program consists of three components: Public Safety Building, Neighborhood Fire Stations & Support Facilities, and Auxiliary Water Supply System. In this reporting period, under the Neighborhood Fire Stations, Station 16 achieved final completion and Station 5 completed construction. Additional Focused Scope category projects within the Neighborhood Fire Stations component are proceeding apace, adhering to stipulated schedules and budgets.

The \$400 million Earthquake Safety and Emergency Response 2014 (ESER 2014) Bond Program consists of five components: Office of the Chief Medical Examiner, Traffic Company & Forensic Services Division, Neighborhood Fire Stations, Emergency Firefighting Water System, and Police Facilities.

The *Office of the Chief Medical Examiner* project was inaugurated in November 2017 and is fully operational. The Executive Architect's final payment is pending LEED Gold certification which is under review by the U.S. Green Building Committee (USGBC).

At the CPC meeting of 4/30/18, Capital Planning staff directed the ESER Program Manager to suspend four (4) ESER 2014 projects – 2 police and 2 fire – to approximate the \$8.645M needed to align with the modified *Traffic Company & Forensic Services Division* project scope. These projects will remain suspended until the trade bid packages are largely bought-out and the true TCFSD budget deficit understood, expected to occur in December 2019 to early 2020.

Under *Neighborhood Fire Stations* component, demolition activities started at Pier 22 ½ for *Fireboat Station 35* and the *Focused Scope* category projects are proceeding apace, adhering to stipulated schedules and budgets.

The Police *Northern, Taraval, and Richmond Station Renovation Project* is scheduled to be completed in January 2020; work at Park and Ingleside will be completed by January 2020; work at Bayview and Tenderloin Project is projected to be finished by February 2020.

The Public Utilities Commission manages the projects under the *Auxiliary Water Supply System* and the *Emergency Firefighting Water System* components for both programs. Construction continued for Ashbury Bypass Pipeline (2500J) and Pumping Station 2 (WD-2687) contracts. Contract bidding advertisement expected in January 2020 for Clarendon Supply Pipeline (WD-2861) and February 2020 for 19th Ave Pipeline (2652J). Bids for Terry Francois Boulevard/Mission Rock/Warriors Way Pipeline (DB-129.1) being evaluated.

To date, the ESER 2010 program has received the proceeds of six bond sales totaling \$412,300,000 and in addition has received interest earned with a current total appropriation of \$415,372,929. The ESER 2014 program has received the proceeds of three bond sales totaling \$397,988,157, inclusive of savings from cost of issuance which has been appropriated to the other program components.

Please refer to the following report for further details or visit the ESER website at www.sfearthquakesafety.org for previously issued reports.

Program Summary and Status

Public Safety Building (ESER 2010)

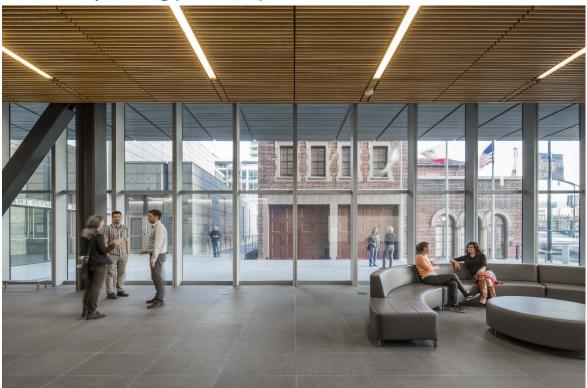


Photo © Tim Griffith, 2015

Location: Block 8 in the Mission Bay South Redevelopment Area. The block is bounded by Mission Rock, Third, and China Basin Streets.

Project Description: The Public Safety Building (PSB) is meant to provide a new venue for the SFPD Headquarters – effectively the command and control administration of the City's police department-including the relocation of Southern District Station and a new Mission Bay Fire Station. Included in the project is the reuse of Fire Station #30, which will serve as a multipurpose facility for the Fire Department and the community. Historic resource consultants have determined that the existing fire station is eligible for the National Register of Historic Places. Consistent with the Mission Bay SEIR Addendum No. 7, Mitigation Measures, Item D.02, this facility will be retained and reused in a manner that preserves its historic integrity. The other components of the project will be designed to be respectful of the historic integrity of the existing fire station.

Project Background: The functionality of the entire police department in the event of a major catastrophe relies on the ability of the police leadership within police command center

headquarters to promptly and properly coordinate public safety services in the city. The district station plays an equally critical role in providing responsive public safety to residents of San Francisco in a timely manner. This station includes those working the front line that are the first to arrive at a crime scene, maintain the peace during difficult situations, assist in the investigation of criminal activity; provide support to other first responders including the Fire Department and emergency medical services.

Project is complete and the facility is occupied.

Project Budget: Project Cost, inclusive of all change orders to date, tracked to within the Total Project Budget of \$243M (GO Bonds and general funds).

Neighborhood Fire Stations (ESER 2010)

Component Description: The ESER bond will renovate or replace selected fire stations to provide improved safety and a healthy work environment for the firefighters. The selected stations are determined according to their importance for achieving the most effective delivery of fire suppression and emergency medical services possible.

Background: All of the 43 San Francisco Fire Stations have, as a result of minimal deferred maintenance over decades, yielded building conditions that potentially compromise the safety and health of firefighters. Many stations have structural/seismic and other deficiencies that could inhibit their continuous functionality. Some may not be operational after a large earthquake or other disasters, hindering the ability of the firefighters to respond to calls for service.

Prior to approval of the bond program, the majority of the City's fire stations and support facilities were generally assessed for their respective condition and to identify vulnerabilities or deficiencies that could compromise their essential role as deployment venues for first responders.

For budget planning purposes, the assessment reports were reviewed by cost estimators who prepared estimates of the cost of correcting the conditions noted in the assessments. The cost estimates indicate only the overall "order of magnitude" of the various facility deficiencies and relative proportions of various types of work.

Preliminary assessment of the neighborhood fire stations indicate that the sum of all existing deficiencies would require a budget exceeding \$350M to correct, significantly more funds than are available in this bond for such purposes. Therefore, additional detailed planning is required to focus the expenditures of this bond towards the most beneficial and cost-effective immediate rehabilitation and/or improvement projects.

A list of projects to be completed by the ESER 2010 bond was identified by Public Works and the Fire Administration and accepted by the Fire Commission at their meeting of September 23, 2010.

The ESER 2010 bond program is anticipated to complete improvements to 24 of the 43 neighborhood fire stations. The approved slate of projects was presented to the SF Fire Commission on April 26, 2012.

In addition, Public Works certified two Master Job Order Contracts (JOC) with specialty door contractors, National Garage Door and Byron Epp, for the remaining Apparatus Bay Door Replacements. ESER 2010 will fund the replacement of apparatus bay doors at ten stations. Scoping and pricing for the work is underway with material procurement anticipated to begin in Fall 2019.

The following is a detailed status per project:

Seismic Projects

Fire Station No. 16 (Marina District)

Design Services:

- Architecture: San Francisco Public Works
- Structural, MEP, and Fire Alarm
 Engineering: San Francisco Public Works
- Civil Engineering: Parsons Brinckerhoff

General Contractor: Roebuck Construction

Schedule: Substantial completion was achieved on January 10, 2019. As a result of the overall delay of the project, Public Works has assessed



Photo © Alejandro Velarde, 2019

liquidated damages from July 17, 2018 to January 10, 2019, in the amount of \$445,000. SFFD began occupying and operating out of the new station on January 16, 2019. A ribbon cutting ceremony was held on January 31, 2019. Final completion was achieved on July 18, 2019.

Fire Station No. 5 (Fillmore District)

Design Services:

- Architecture: San Francisco Public Works
- Structural Engineering: San Francisco Public Works
- MEP, Fire Alarm, and Civil Engineering: GHD

General Contractor: Alten Construction

Schedule: SFFD began occupying and operating out of the station on April 29, 2019. A ribbon



Photo © Alejandro Velarde, 2019

cutting ceremony was held on May 1, 2019. Final Completion is anticipated to be achieved in February 2020.

Fireboat Station 35: (See ESER 2014 this report)

Fireboat Station 35 will occur within ESER 2014 Program, however, the pre-design and CEQA and environmental review costs of \$687,125 occurred under ESER 2010. The budget that was identified for Station 35 was funded by ESER 2010 and the Fire Facilities Bonds funds totaling \$17M. The ESER 2010 funding will be used to offset Station 5 and 16. The Fire Facilities Bond funds will continue to supplement ESER 2014 funds for Station 35.

Earthquake Safety and Emergency Response Bond Program

(ESER 2010 & 2014)

Equipment Logistics Center (ELC):

The ELC project was identified after the passage of the bond – it was suggested as a project combining the Bureau of Equipment (BOE) and Emergency Medical Services (EMS). In this configuration, the total functional program area makes it infeasible to occur at the current EMS venue at 1415 Evans; more significantly, the budget for such a project is not available within the ESER 2010 NFS funding.

SFFD requested that Public Works prepare a program analysis and cost estimate for the EMS apart from the BOE for consideration in the proposed 2016 Public Health and Safety Bond – which received 79 percent voter approval in June 2016.

Comprehensive Project: Station 36

Project was successfully completed and SFFD reoccupied the station on November 19, 2014.

Focused Scope Projects

Design services:

- Public Works BDC/IDC for Roofing, Envelope, Apparatus Bay Door Replacement, Showers, and Sidewalk categories of Focused Scope.
- GHD (as-needed electrical engineering consultants) for Generator Replacement projects.

Roofs – 15 Stations

Summary: The scope consists of installing new roofing systems and upgrading exhaust fans on fifteen (15) stations. 2011 Package (Stations 6, 38, 41 and 42), Package 1 (Station 28); Package 2 (Station 2); Package 3 (Stations 18, 40 and 31), Package 4 (Stations 15, 17, 26, and 32), and Package 5 (Stations 10 and 13) roofs. Per SFFD direction, the 2011 package and Package 2 were completed by JOC contractors, and the balance of the projects were bid out to C39 roofing contractors.

Detail: All work is complete.

Exterior Envelope (BBR) - 16 Stations

Summary: The scope consists of paint and ancillary work to prevent water intrusion at sixteen (16) stations. Per SFFD direction, BBR executed the paint work at six (6) Stations, 6, 28, 38, 41, 42, and 49 while the remaining work, Package 4 (Stations 15, 32 and 40), Package 5 (Stations 10, 13, 17 & 26), and Package 6 (stations 2, 18 & 31) were bid out through Public Works public bidding process to B or C33 license contractors due to the complexity of scope at these stations.

Detail: All work is complete.

Earthquake Safety and Emergency Response Bond Program

(ESER 2010 & 2014)

Emergency Generator Replacement – 5 Stations

Summary: The scope consists of installing new Emergency Generators and related ancillary scopes of work at five (5) Stations 6, 12, 15, 17, and 21. Per SFFD direction, BBR executed the work at Station 15; a JOC contractor executed the work at Station 17; and Stations 6, 12 and 21 were bid through the Public Works public bidding process to C10 license contractors.

Detail: All work is complete.

Shower Reconstruction – 9 Stations

Summary: The scope of work consists of installing new shower stalls including shower pans, shower heads, divider walls, glass doors, floor drains, p-traps, access panels, and ancillary scopes of works at nine (9) Stations, 6, 13, 15, 17, 18, 26, 38, 40 & 41. Station 6 was completed by BBR in July 2013. Station 15 was completed by JOC Contractor, Rodan Builders, in September 2013. Stations 13, 18, 26, 38, 40 & 41 were bid through the Public Works public bidding process to B license contractors. Stations 17 and 18 were put on hold by SFFD due to scope complexity.

Detail: All work is complete.

Mechanical Scope (JOC) – 15 Stations

Summary: The scope is structured into two phases: Phase 1 – Investigation and Scope Validation, and Phase 2 – Execution of Work. The stations were divided into two groups, Group 1 – four (4) stations and Group 2 – eleven (11) stations. Group 1 (Stations 6, 17, 38 and 42) had an NTP issued on May 24, 2013. The stations were substantially completed in August 2013, and final completed by Azul (JOC Contractor) in November2013. Group 2 (Stations 2, 10, 13, 15, 18, 26, 28, 31, 32, 40, 41) were awarded to Rodan (JOC Contractor). NTP was issued on December 16, 2013. Work started on January 2, 2014 and reached final completion in November 2014.

Detail: All work is complete.

Window Repair (BBR) - 12 stations

Summary: The scope consists of installing new latch, handle, weep holes, sealant and weather-strip to existing windows, replacing broken panes of glasses, and adjusting alignment and resealing the perimeter of the frame to water tight at twelve (12) Stations, 2, 6, 17, 25, 26, 28, 31, 32, 38, 40, 41 and 42. BBR was selected to perform the work per SFFD direction. The first Package including Stations 28, 38, 41 and 42 started in April 2012 and completed in June 2012; the second package including Stations 6, 17, 32 and 40 began in April 2013 and finished in June 2013; and the third package including Stations 2, 25, 26 and 31 started construction in November 2013, and completed in January 2014.

Detail: All work is complete.

Additional Focused Scope

Summary: Additional Focused Scope includes Apparatus Bay Door Replacement at multiple Fire Stations and Exterior Envelope Painting at Fire Department Headquarters. In addition, in July 2017, SFFD requested that additional Fire Stations receive Additional Generator Replacements. The funding allocated for Additional Generators will be applied toward a prioritized list of Fire Stations selected by SFFD.

Detail:

- Emergency Generator Replacement 1 Station (FS 14)
 Plans were submitted to DBI for building permit on November 25, 2019.
- Apparatus Bay Door Replacement 9 Stations
 National Garage Door (NGD) received NTPs for all Fire Stations: (1) Stations 8 and 28 on 10/21/19, (2) Stations 14, 18, 20, and 26 on 11/25/19 and (3) Stations 33, 39, and 43 on 10/28/19. Procurement of doors is underway and Final Completion of all stations will occur on or before 5/10/20.
- Exterior Envelope SFFD Headquarters All work is complete.

Project Budget:

Refer to the Attachment 1 – Program Budget Report.

Neighborhood Fire Stations (ESER 2014)

Component Description: The ESER 2014 bond program continues the work of ESER 2010 bond, categorizing projects according to three sub - categories of Focused Scope, Comprehensive, and Seismic. The ESER 2014 bond program will continue to address identified and prioritized needs at Fire Stations that were previously not addressed under the 2010 program. Significant construction projects will have been completed at all SFFD Fire Stations at the conclusion of the 2010 and 2014 bond programs.

SFFD approved the NFS Focused Scope, Comprehensive and Seismic budget portfolio in April 2015. In October of 2017, SFFD approved an updated budget revision.

Design services are being provided by Public Works Bureaus of Architecture & Engineering, unless otherwise noted.

The following is a detailed status per project:

Seismic Projects:

Fireboat Station 35 at Pier 22 ½



Embarcadero Perspective of West and South Elevations

Design-Builder: Swinerton-Power, a Joint Venture and Shah Kawasaki Architects

FLOAT (float, steel piles, observation deck, vehicle access platform, gangway)

Design Phase: October 2017 – November 2018 PORT Permits: November 2018 – July 2019 Construction Phase*: July 2019 – January 2020

*Fabrication of float through delivery to Treasure Island; includes demolition activities at Pier 22 ½.

BUILDING

Design Phase: October 2017 – July 2019 PORT Permits: March 2019 – November 2019 Construction Phase*: January 2020 – January 2021

*Construction of building superstructure on top of float at Pier 1, Treasure Island and pile driving activities (guide piles for float and piles for public access platform) at Pier 22 ½.

The Port issued permits for fabrication of the float and other steel elements (piles, observation deck, vehicle access ramp, gangway) and demolition activities on July 25, 2019 and August 19, 2019, respectively. Building permit was issued on November 22, 2019.


Pier 26 Fireboat Berths

Design services: COWI North America

Contractor: Vortex Marine Construction

Percentage complete (as of 8/31/2019): 99%

Delays to construction are due to unforeseen conditions during excavation of the Embarcadero sidewalk, which required the relocation of two conduits. Additional delay due to rain prevented the placement of the concrete sidewalk as scheduled. Difficulties in timely coordination of electrical work and inspections with PG&E



Fireboat No. 3, the Saint Francis, moored at Pier 26

was a major factor that contributed to the delay. The switchgear was inspected and approved to energize by PG&E on December 6, 2019. Remaining electrical work to be completed by mid-February 2020.

Comprehensive Projects:

Fire Station 3 & 7

FS 3 was determined to be a potential collapse hazard in the event of a major earthquake based on the structural assessment received from the Public Works IDC-Structural study. SFFD directed the design work to stop and will consider plans for a new FS 3 in its overall seismic portfolio of future bonds. FS 7 is on hold, since a complete rebuild is being considered as part of the ESER 2020 bond program.

Focused Scope Projects:

The NFS team has moved forward with planning, design, bidding and construction of the Focused Scope projects in all 9 of the categories: apparatus bay doors, roof replacements, shower renovation, exterior envelope, windows, sidewalk, emergency generator, and mechanical projects. ESER 2014 Focused Scope projects upgrade 35 Fire Stations in these categories.

Design services are being provided by Public Works BDC Architecture, IDC Mechanical and IDC Structural for Roofing, Envelope, App Bay Door Replacement, Showers, Windows, and Sidewalk categories of Focused Scope. GHD, an as-needed electrical engineering consultant, is providing design services for Generator Replacement projects.

Apparatus Bay Doors (37 Fire Stations):

Design has been completed by Public Works BDC Architecture for the Apparatus Bay Door Replacement projects at all remaining fire stations. Work will be divided between ESER 2010 and ESER 2014, within parameters of allocated budgets under each bond.

- Package 1 (FS 15; including Ancillary Work)
 This project is complete.
- Package 2 Ancillary (not used)
 Ancillary work is now tracked under "Package 4".
- Package 3 App Bay Door Replacement (Apparatus Bay Doors at FS 2, 11, 13, 19, 24, 31, 34, 40, 41) is complete.
- o Emergency Declaration Fire Station 3 is complete.

Package 4 Ancillary Work for new 4-Fold Doors (FS 6, 9, 10, 11, 12, 14, 17, 20, 21, 22, 23, 26, 32, 37, 38, 42, 44) is complete.

Earthquake Safety and Emergency Response Bond Program

(ESER 2010 & 2014)

o Package 5:

The scope is to replace existing app bay doors with new telescoping and coiling overhead doors at multiple Fire Stations. (5) NTPs have been issued to JOC Byron Epp, and procurement is underway to replace app bay doors at 15 Fire Stations (FS 6, 7, 9, 10, 11, 21, 22, 38, 25, 37, 42, 17, 23, 32 & 44). Final Completion is anticipated on June 1, 2020.

Roofs (10 Fire Stations):

All projects in the Focused Scope Roofing category have been completed.

- Package 1 (FS 3 Roof/HVAC/Generator Replacement)
- Package 2 (FS 40 Roof Replacement In-kind)
- Package 3 (FS 3 & 17 Roof Replacement)
- Package 4 (Not Used)
- Package 5(FS 9, 20, 23, 24, 29, & 43).

Showers (7 Fire Stations):

- Package 1 (FS 13, 20, 22 & 34) is complete.
- Package 2 (FS 17, 19 & 33):
 The scope is to renovate the existing showers at 3 stations. This project was bid on October 23, 2018, and an NOA was issued to Kushner General on December 7, 2018. Substantial Completion was achieved on August 5, 2019, and this project is completed. Final Completion was achieved on September 19, 2019.



Window Repairs (13 Fire Stations):

BBR was selected to perform all the work, per SFFD direction, for all window repair projects. All projects are complete:

- o Package 1 (FS 9, 19, 24, & 29)
- Package 2 (Not Used)
- o Package 3 (FS 25)
- Package 4 (FS 8, 20 & 21)
- Package 5 (FS 14, 33, 37 & 43):

FS 14, 37, and 43 are completed, and FS 33 sliding door project has been cancelled due to obsolescence of repair parts. FS 33 sliding doors will be considered for replacement in a future bond.

o Package 6 (FS 11, 12 & 23)

Exterior Envelope (8 Fire Stations):

- Package 1 (FS 8, 20, 23 & 29):
 The scope includes power wash and new paint to exterior facade of the stations. BBR was selected to perform the work per SFFD direction.
 - o In November 2018, BBR completed work at FS 20.
 - o In November 2019, BBR completed work at FS 8
 - o In November 2019, BBR commenced with work on FS 29.
 - BBR has refused work at FS 23 in this package. A JOC will be procured for work at FS 23 in 2020.
- o Package 2 (FS 24 & 34) is on hold until late 2019.
- Package 3 (FS 11):
 - The scope of work includes repair deficiencies at the exterior envelope, power wash all surfaces, and prepare substrates required to receive new paint at the exterior façade. This project will be folded into the Seismic Hose Tower Removal project, a project that is funded by the 2016 Public Health and Safety Bond and is anticipated to bid in early 2020.
- o Package 4 (FS 22) is complete.

Mechanical (TBD)

Package 1 (8, 9, 14, 20 & 41):
 Per discussion with BBR, BBR team may be able to diagnose and improve the rooftop mechanical units at various stations. Previous PM met with BBR on 9/23/16 to discuss work logistics and plan. Mechanical scope of work at each station will be confirmed during site walks with BBR in 2019, and priorities will be assigned in discussions with SFFD.

Emergency Generators:

Package 1 (FS 31):

The original project included replacement of the generator at FS 31, and minor improvements at FS 14, 24 and 37. At SFFD's request, the repairs at FS 14, 24, and 37 have been cancelled as part of this project. Instead, the SFFD requested full replacement of generators at FS 14, 24, and 37.

Package 1 scope of work is to replace the existing emergency generator at FS 31 with a new

generator and fuel tank to meet SFFD's 72-hour emergency run time protocol. On June 13, 2019, Public Works awarded a contract for \$219,331 to BBJ Electric, an as-needed electrical contractor. On July 16, 2019, a pre-construction meeting was held. NTP was issued on August 5, 2019. This work is anticipated to be completed in January 2020, ahead of the Final Completion date of April 2020.

Additional Generator Replacement at FS 2:

The scope of work consists of replacement of an existing roof top generator with a new generator, structurally strengthen the roof to support the new fuel tank with capacity for 72-hour run time and provide new fuel fill port and piping to the generator. On August 15, 2019 DBI permit was obtained.

On November 20, 2019, this project was informally bid to a pool of As-Needed contractors. The bid results exceeded the \$600k limit allowed under informal bid procurement. This project has been repackaged with additional generator projects and bid preparation for advertising is underway for a formal contract for bid.

Additional Generator Replacement at FS 19:

The scope of work will consist of replacement of an existing generator with a new generator and fuel tank to meet SFFD's 72-hour emergency run time protocol. In addition, GHD has recommended the replacement of infrastructure components including existing electrical switchgear, transfer switch, distribution panel board, and new feeders. This project is being packaged with FS 2 Generator and advertisement for the Invitation to Bid is anticipated in early January 2020.

Sidewalks/Slabs

All projects in the Focused Scope Sidewalk:

- o Package 1 (FS 13) is complete.
- o Package 2 (FS 31) is complete.
- Package 3 (FS 26) is complete.
- Package 4 (FS 20) was eliminated at SFFD's request.

Access Control Systems (35 Fire Stations):

The scope is to ensure the safety and security of personnel, apparatus and equipment at all fire stations by providing electronic access control systems via card key at exterior persondoors at all fire stations, including replacement of door hardware and electronic equipment as needed. Thirty-three Fire Stations have received new electronic access control systems, and 11 Fire Stations are remaining.

This work is complete.

Bureau of Equipment and Emergency Medical Services

SFFD requested Public Works to prepare a program analysis and cost estimate for the Bureau of Equipment (BOE) and the Emergency Medical Services (EMS) for consideration as a project or projects to be funded by ESER 2014.

The two projects were found to be infeasible to deliver within ESER 2014.

The EMS Facility project was deferred to Public Health and Safety Bond which was approved by 79 percent of the voters in June 2016 under the new project name of Ambulance Deployment Facility (ADF). Public Works completed program analysis and conducted test fits for the EMS Facility at four locations. The optimal site was found to be a consolidation of two properties owned by the City, the equipment yard located behind Fire Station No. 9, at 2245 Jerrold Ave., combined with an adjacent vacant railroad right-of-way that extends from Jerrold Avenue to McKinnon Avenue. The budget for the EMS Facility is \$44M, for a project scheduled to be completed in 2020.

Public Works conducted test fits of the BOE Facility at two locations. The optimal scenario was found to be renovation of the existing SFFD EMS facility at 1415 Evans, which would become available after EMS is relocated. Therefore, further work on the BOE Facility project is deferred to a subsequent bond program to be determined.

Earthquake Safety and Emergency Response Bond Program

(ESER 2010 & 2014)

Emergency Firefighting Water System

Component Description: The Earthquake Safety and Emergency Response Bonds will seismically improve the Emergency Firefighting Water System cisterns, pipelines, tunnels, and physical plant.

Background: The Emergency Firefighting Water System is vital for protecting against the loss of life, homes, and businesses from fire following an earthquake. It is also used for the suppression of non-earthquake multiple-alarm fires.

Status:

Planning and Design

- 1. Lake Merced Pipeline Install new 20" AWSS pipe from Lake Merced Pump Station to Vidal Drive / Higuera Avenue intersection. Design completion 6/2020.
- 2. Westside Potable EFWS Pipeline Install new Potable Emergency Firefighting Water System pipeline in Richmond and Sunset areas. Planning completion 4/2020.

Construction

- 3. 19th Avenue Pipeline Install new 20" Auxiliary Water Supply System (AWSS) pipe on 19th Avenue from Irving Street to Kirkham Street as part of Public Works' 19th Avenue Roadway Improvements, Contract 2652J. Bids due 2/2020.
- 4. Terry Francois Blvd/Mission Rock/Warriors Way Pipeline Install new 20" AWSS pipe on Terry Francois Blvd from Mission Rock Street to Warriors Way as part of SFPUC contract DB-129.1. Bids being evaluated.
- 5. Ashbury Bypass Pipeline Install new 20" AWSS pipe near Ashbury Heights Tank as part of Public Works' Clayton St, Clipper St, and Portola Dr. Pavement Renovation, Sewer Replacement and Water Installation, Contract 2500J. AWSS construction completion 2/2020.
- 6. Clarendon Supply Provide a new AWSS water supply and pipe near the crest of Clarendon Avenue at Dellbrook Avenue. Bid advertisement 1/2020.
- 7. Pumping Station 2 Improve the building structure's seismic performance. Construction completion 12/2020.
- 8. Street Valve Motorization Motorize street valves on AWSS pipelines for improved water flow control. Construction completion 12/2020.

Office of the Chief Medical Examiner (OCME)



Project Description: The project will relocate the Office of the Chief Medical Examiner (OCME) to One Newhall Street in the India Basin Industrial Park. The new facility will house about 50 employees who are organized into the four units of the OCME: Field Investigations, Medical/Autopsy, Laboratory, and Administration.

One Newhall Street was an existing 28,000 gsf industrial warehouse which was almost entirely demolished, and a second floor was added within the existing footprint of the building resulting in a seismically safe 46,000 gsf facility.

Background: The existing OCME is located at 850 Bryant also known as the Hall of Justice (HOJ). The HOJ is over 50 years old and seismically deficient. In the event of a major earthquake, this building is not expected to be operational. This project is part of a larger strategy to replace the Hall of Justice established in the City's 10-Year Capital Plan as the Justice Facilities Improvement Program (JFIP).

The OCME is accredited by the National Association of Medical Examiners (NAME). During the previous accreditation in 2008, the City was advised that the existing facility is undersized, has

multiple deficiencies that are currently mitigated by operational protocols, and the facility should be replaced to assure continued accreditation.

Project Status:

LEED Gold is the mandatory goal for this project (minimum 60 points required to be awarded for the Gold certification). Project was registered with USGBC on April 9, 2014. Out of submitted 64 points, USGBC awarded 52 points to the project; 6 points have been submitted for review; 2 points are being prepared for submission in January 2020.

Project is complete and the facility is occupied. Project Budget: Project Cost, inclusive of all change orders to date, tracked to within the Total Project Budget of \$75M (GO Bonds and general funds).



Traffic Company & Forensic Services Division (ESER 2014)

Aerial Photo of 1995 Evans Avenue Post-Demolition (2018)

Project Description: The project will relocate the SFPD Forensic Services Division (FSD) and SFPD Traffic Company (TC) to a site located at 1995 Evans Avenue, San Francisco. The amount of space requested for the Traffic Company was determined based on the Police Facilities Master Planning Study dated August 23, 2012.

The project is being developed to support a Full Time Employee (FTE) forecast for 2020 FSD demand of approximately 109 for FSD, approximately 100 for the Traffic Company and approximately 9 for the Real Estate Division's building engineering and custodial services. The size of the facility is approximately 100,000 gross square feet and allows for a potential future expansion if required.

Project Background: The SFPD Traffic Company is currently located at the Hall of Justice (HOJ) at 850 Bryant Street. The SFPD FSD is currently located in two facilities. The FSD Administration, Crime Scene Investigations, and Identification units are housed at the HOJ. The FSD Crime Lab is housed in Building 606 at the Hunters Point Shipyard.

The HOJ is over 50 years old and seismically deficient. In the event of a major earthquake, this building is not expected to be operational. This project is part of a larger strategy to replace the

Hall of Justice, established in the City's 10-Year Capital Plan as the Justice Facilities Improvement Program (JFIP).

The Hunters Point Shipyard is being transferred from the U.S. Navy to the City. The City plans to develop the Shipyard as a residential area. The area in which Building 606 is located is planned to be public open space as an amenity for nearby residences. Prior to the transfer of the property, the Navy is obligated to remove and mitigate hazardous materials in the soil.

Project Status: DBI issued the Demolition Permit on May 8, 2018. Additional existing below grade foundation remains were discovered in July, August and September delaying completion of demolition until the fourth quarter of 2018. The Site Permit application was submitted to DBI on December 21, 2017 and was issued on December 5, 2018, inclusive of the various approvals required from Planning, DBI, SFFD, DPH and BSM. A five-month review duration was anticipated to obtain the Site Permit, which took nearly 12 months, resulting in further delay to subcontractor procurement and construction activities. Attempts to mitigate these delays include a commitment from DBI to assist in expediting the permit addendum schedule. Some success has been realized, with the deep foundation addendum S1 submitted to DBI on December 14, 2018 and issued by DBI on April 3, 2019. The foundation and superstructure addendum S2 were submitted to DBI on March 7, 2019 and was approved on July 23, 2019. The 95% Construction Documents milestone was reached on August 26, 2019. From this several permit addenda were submitted to DBI on August 27, 2019. These addenda were S3: Building & MEP, S4: Fire Sprinkler and S5: Fire Alarm. Addendum S6: Emergency Responder Radio Communication System was submitted on September 24, 2019.

Clark Construction was selected to be the Construction Manager/General Contractor (CM/GC) through a competitive solicitation in July 2017. Clark leads a team of "Core Trade Subcontractors," specifically: C/S Erectors for the exterior building envelope, Southland Industries for mechanical and plumbing, and Rosendin Electric for electrical. Their Preconstruction initial estimate in January 2018 reported a nearly \$30M over budget amount. Cost reduction efforts were presented to the Capital Planning Committee (CPC) on April 30, 2018. The presentation described that after two separate value-engineering (cost reduction) efforts yielding reductions of \$12.35M + \$14.3M without diminishing adversely the integrity of the program, and inclusive of additional bond generated funding of \$8.7M made available to the TCFSD, the \$6.65M budget deficit remained. When factoring appropriate contingency to this \$6.65 million budget deficit, it has produced an \$8.65 million deficit in funding. The resulting outcome of the CPC meeting, Capital Planning staff directed the ESER Program Manager to suspend four (4) ESER 2014 projects – 2 police and 2 fire – to approximate the \$8.645M. These projects will remain suspended until such time as the trade bid packages are largely bought-out and the true TCFSD budget deficit understood, expected to occur in December 2019 to early 2020.

As of December 2019, approximately 80% of the estimated cost of work has been bid and procured, including the MEP and exterior enclosure scopes represented by the design-build Core Trade Subcontractors. The indicator pile program was successfully completed allowing new construction to begin on October 7, 2019. Deep foundation pile installation was completed in December 2019 with mud slab and waterproofing following. The mat slab construction will take place starting in late December 2019 and into the first quarter of 2020.

The project is obligated to achieve LEED Gold certification.

Schedule:

- Pre-Construction Services NTP
- Pre-Construction Services Full Team Kick-off Meeting
- Indicator Pile Program construction Services NTP
- New building construction Services NTP
- Substantial Completion
- Final Completion

November 27, 2017 November 30, 2017 August 19, 2019 October 7, 2019 October 2021 Fall 2021

Earthquake Safety and Emergency Response Bond Program

(ESER 2010 & 2014)

Police Facilities (ESER 2014)

Component Description: The project includes various focused scope projects at 12 police facilities (9 district stations and 3 support facilities) across the City. The work scopes are derived from a series of onsite investigations, observations, and professional evaluations of different building systems that include mechanical, electrical, plumbing, fire protection, and structural safety. It also includes assessments of building envelope (i.e. integrity of roof, doors, windows, and walls), ADA accessibility requirements, as well as other site improvements that ensure safety and security.

The project's overall budget is \$30M, the cost to address all building issues will likely exceed the budget, and therefore priorities are selected per recommendations by the Citywide Capital Plan. Those building deficiencies that potentially compromise the public's health and safety, and others that pertain to code compliance will get the priority.

ADA PACKAGE 1

The project addresses accessibility issues at the following stations: Central, Mission, Bayview, Northern, and Tenderloin.

ADA PACKAGE 2

The project addresses accessibility issues at the following stations: Park, Ingleside, Taraval, Richmond, and Police Academy.

NEW FIREARMS SIMULATOR TRAINING FACILITY at Lake Merced

This project is completed, there are no updates.

NORTHERN, RICHMOND, TARAVAL POLICE STATION RENOVATION PROJECT

Projected substantial completion is January 2020.



New roof-top supply fan. Quarterly Status Report

Richmond Station:

1. Awaiting Final Building Inspection.

Northern Station:

- 1. Conduct functional testing by Yum's Mechanical in the week of January 6, 2020.
- 2. Test, balance, and commission HVAC system.
- 3. Schedule punchlist back-check walk.

Taraval Station:

1. Testing and Air Balancing (TAB).

PARK and INGLESIDE POLICE STATION RENOVATION

PARK STATION

1. Work is completed.

INGLESIDE STATION



New generator and belly tank.

Rafter tail replacement.

- 1. Working on programming of the HV-1, HV-2 and AHU mechanical units.
- 2. Pending Fire Alarm testing for the duct detectors.
- 3. Pending completion of the Air Balancing.

MEP PACKAGE 2 (BAYVIEW, TENDERLOIN)

TENDERLOIN STATION

- 1. Substantial completion pending sign off from DBI Electrical and the SFFD District Inspector (requests made for fire egress improvements).
- 2. Contractor working on punchlist items.

BAYVIEW STATION

- 1. Generator fuel line pipe in the parking lot installed (replacement of existing generator fuel lines).
- 2. Approval from the Dept. of Public Health is pending DPH permit processing and inspection. Thereafter, backfill and compaction can proceed.
- 3. Contractor working on pre-substantial punchlist items.

POLICE ACADEMY RENOVATION

This project is on-hold per CPC.

MISSION POLICE STATION RENOVATION

This project is on-hold per CPC.

Budget, Funding and Expenditures

ESER 2010

The budget for the ESER 2010 Bond Program is \$412,300,000. The revised budget is \$415,372,929 which includes interest-earned. The following is a summary of the budget and appropriation per component:

ESER 2010: As of December 2019

Bond Components and Projects	Bond Authorized Amount	Revised Budget (ii)	Appropriations	Expenditures	Encumbrances	Balances	Expenditures/ Appropriations
Public Safety Building (PSB) (iii)	239,000,000	236,661,975	236,661,975	228,865,318	0	7,796,657	97%
Neighborhood Fire Stations (NFS)	64,000,000	66,906,313	66,906,313	64,628,750	1,184,845	1,092,718	97%
Auxiliary Water Supply System (AWSS)	102,400,000	102,400,001	102,400,001	88,527,602	5,646,010	8,226,389	86%
Oversight, Accountability & Cost of Issuance	6,900,000	2,545,864	2,545,864	2,074,056	0	471,807	81%
Public Works Program Reserve		2,443,743	2,443,743	0	0	2,443,743	0%
Appropriated Unallocated Interest		4,415,033	4,415,033	0	0	4,415,033	0%
TOTAL (i)	412,300,000	415,372,929	415,372,929	384,095,727	6,830,855	24,446,347	92%

⁽i) PeopleSoft financial data thru Q2 FY2020

The Accountability reports for the second thru sixth bond sales are available on the ESER website at http://www.sfearthquakesafety.org/eser-reports.html.

Expenditures and Encumbrances

The ESER 2010 expenditures and encumbrances are \$384,095,727 and \$6,830,855 respectively. Expenditures represent 92% of the total current appropriations.

⁽ii) Revised budgets based on PeopleSoft appropriations; data subject to change per clean-up efforts

⁽iii) Estimated savings included in project balance; project financial close out in process

ESER 2014

The ESER 2014 budget is \$400,000,000 and the total appropriation is \$397,988,157, including a savings from the cost of issuance currently allocated within program components. The following is a summary of the budget and appropriation per component:

ESER2014: As of December 2019

Bond Components and Projects	Bond Authorized Amount	Revised Budget (ii)	Appropriations	Expenditures	Encumbrances	Balances	Expenditures/ Appropriations
Office of the Chief Medical Examiner (OCME)	63,895,000	67,533,024	67,533,024	67,383,416	41,914	107,693	100%
Traffic Company & Forensic Services Division (TC/FSD)	162,195,000	163,375,150	163,375,150	45,344,911	65,349,058	52,681,181	28%
Police Facilities (PF)	29,490,000	29,645,661	29,645,661	24,077,669	825,992	4,742,000	81%
Neighborhood Fire Station (NFS)	83,555,000	80,351,381	80,351,381	29,397,217	26,012,553	24,941,612	37%
Emergency Firefighting Water System (EFWS)	54,065,000	54,347,209	54,347,209	25,643,303	11,479,210	17,224,696	47%
Oversight, Accountability & Cost of Issuance	6,800,000	2,284,545	2,284,545	1,590,562	0	693,983	70%
Public Works Program Reserve		451,187	451,188	0	0	451,188	0%
TOTAL (i)	400,000,000	397,988,157	397,988,157	193,437,079	103,708,727	100,842,352	49%

⁽i) PeopleSoft financial data thru Q2 FY2020

The Accountability reports for the second and third bond sales are available on the ESER website at http://www.sfearthquakesafety.org/eser-reports.html.

Expenditures and Encumbrances

The ESER 2014 expenditures and encumbrances are \$193,437,079 and \$103,708,727 respectively. The expenditures represent 49% of the total current appropriations.

⁽ii) Revised budgets based on PeopleSoft appropriations; data subject to change per clean-up efforts

Earthquake Safety and	Emergency	Response	Bond	Progra	m
		(ESEF	R 2010	& 201	4)

Attachment 1 – Contact Information



San Francisco Public Works | City and County of San Francisco | Building Design and Construction | Project Management 30 Van Ness Avenue, Suite 4100 | San Francisco, CA 94102 | (415) 557-4700 | sfpublicworks.org

Contact	Title	Component	Telephone No.	Cell No.	E-mail
Charles Higueras	Program Manager	ESER 2010 & 2014	(415) 557-4646	(415) 307-7891	charles.higueras@sfdpw.org
Magdalena Ryor	Project Manager	ESER 2010 NFS; ESER 2014 OCME, NFS, PF	(415) 557-4659	(415) 602-0930	magdalena.ryor@sfdpw.org
Michael Rossetto	Project Manager	ESER 2014 TC/FSD	(415) 557-4773	(415) 530-7368	michael.rossetto@sfdpw.org
Lisa Zhuo	Project Manager	ESER 2014 PF	(415) 557-4699		lisa.zhuo@sfdpw.org
Sherry Katz	Project Manager	ESER 2010 & 2014 NFS Focused Scope	(415) 557-4718		sherry.katz@sfdpw.org
Sean O'Brien	Project Mgr. Asst.	ESER 2010 & 2014	(415) 557-4694		sean.obrien@sfdpw.org
Kelly Griffin	Financial Analyst	ESER 2010 & 2014	(415) 557-4667		kelly.griffin@sfdpw.org



Public Utilities Commission

525 Golden Gate Avenue | San Francico, CA 94102

Contact	Title	Component	Telephone No.	Cell No.	E-mail
David Myerson	Project Manager	ESER 2010 AWSS & ESER 2014 EFWS	(415) 934-5710		dmyerson@sfwater.org

Attachment 2 – Schedule

EARTHQUAKE SAFETY EMERGENCY RESPONSE BOND PROGRAM Timeline and Schedule

		0.1	edule		FY 11/	/12			FY 12/	13			FY 13/	/14			FY 14/	/15	FY	15/16		ı	Y 16/17			FY	17/18			FY	/ 18/19			FY 1	9/20
Description	BUDGET	Scn			, 2011	June 3		July 1,		June 30,		July 1, 20		June 30,		July 1, 201	14	June 30, 2015	July 1, 2015	June 30		July 1, 2016		30, 2017		1, 2017		30, 2018		1, 201 8		30, 2019		1, 2019	June 30, 202
		Start	Completion											3rd Qtr. 4				3rd Qtr. 4th Qtr.	1st Qtr. 2nd Qtr 9/30/15 12/31/15		4th Qtr.	1st Qtr. 2nd Q							r. 1st Qtr.						3rd Qtr. 4th 3/31/20 6/30
NEIGHBORHOOD FIRE STATIONS COMPREHENSIVE: STATION 36				3/30/11	1231111	3/31/12	0/30/12	3/30/12	1231/12	3/31/13	0/30/13	30/13 12	231/13	3/31/14	0/30/14	3130/14 12/	131114	3/31/13	Substantial (0/30/10	3/30/10 12/3//	10 3/3///	0/30/11	3/30/11	12/3///	3/31/10	0/30/10	Final Co		3/3///3	0/30/13	5 5/30/13	1231/13	3/3//20 0/34
Baseline Budget	4,798,218	03/01/12	09/05/14							4,	798,218								12/1/2										9/28/					1	
Current/Approved	5,787,300	03/01/12	09/30/17					-								5,78	37,300		'					-		İ			,						
Current/Projected	5,787,300	03/01/12	12/31/18															5,787								1				¥					
SEISMIC: STATION 5 (New 2-story)																												1			Substan	antial Com	mpletion		
Baseline Budget	13,838,757	03/01/12	05/01/17													13,838,7	757		,						ļ						4	4/29/2019	J		
Current/Approved	21,027,983 (i)	03/01/12	09/12/19																21,027,9	983														4	
Current/Projected	21,027,983 (i)	03/01/12	05/29/19				<u> </u>											:	: :	21,027	7,983				:							*			
SEISMIC: STATION 9 UTILITY ISOLATION Baseline Budget	200,000																																		
Current/Approved	200.000																																		
Current/Projected	200,000																																		
SEISMIC: STATION 16 (New 2-story)																				1										Si Co	ubstantial ompletion		Final Completion		
Baseline Budget	8,841,656	03/01/12	01/04/16										8,8	841,656				-	1 1											1/	/10/2019		7/18/2019		
Current/Approved	14,225,070	03/01/12	05/23/19										Ţ,						14,225,070																
Current/Projected	14,225,070	03/01/12	02/28/20						·	·	·	•	•	·	•		•	·		14,225,070)		·								*		*		

(i) Including \$139,200 FF&E general funds (for built in beds)

Prepared by San Francisco Public Works

EARTHQUAKE SAFETY EMERGENCY RESPONSE BOND PROGRAM

Timeline and Schedule

					FY 10/11			FY	11/12						F	Y 13/14			FY 1	4/15			FY 15	5/16			FY 16	17			FY 17/1	8			FY 18/1	19	FY 19/20					FY 20/21	
Description	BUDGET	Sche	edule	July 1, 2010		ne 30, 2011		1, 2011	June 30		July 1, 2		June 30, 2013		ly 1, 2013		30, 2014	July 1		June 30,		July 1		June 30,		July 1,	2016	June 30,	2017	July 1, 20	17	June 30, 20	018	July 1, 2018	3	June 30, 2019	July	1, 2019	June 30,	2019	July 1, 202	20 .	June 30, 2021
		Start	Completion	1st Qtr. 2nd																							2nd Qtr.			st Qtr. 2n	d Qtr. 3			st Qtr. 2nd 0				2nd Qtr.					Qtr. 4th Qtr.
				9/30/10 12/3		-	1 9/30/11	12/31/11	3/31/12	6/30/12	9/30/12 1	2/31/12 3/	31/13 6/30/	13 9/30/1	13 12/31/1	3 3/31/14	6/30/14	9/30/14	12/31/14	3/31/15	6/30/15	9/30/15	12/31/15	3/31/16	6/30/16	9/30/16	12/31/16	3/31/17	6/30/17	/30/17 12	/31/17 3	31/18 6/	30/18	/30/18 12/31	1/18 3	/31/19 6/30/19	9/30/19	12/31/19	3/31/20	6/30/20 9	/30/20 12/	31/20 3/3	1/21 6/30/21
EMERGENCY FIREFIGHTING WATER SYSTEM (EFV	VS)			PRE-BOND AND DEVE																																							
EFWS (EARTHQUAKE SAFETY EMERGENCY RESPO	NSE 2010)					_																																					
June 2015	102,400,000	07/01/09	09/26/18	,	3	-						*		•	-		10	2,400,00	00	-			-	-	-	*	- 1	-	-														
Baseline	102,400,000	07/01/09	12/31/20		-			1														102.40	0.000															1					
2 (2)								1								1	1				- 1	400.40	0.000			1	1				-		-		-		=						
Current Projection	102,400,000	07/01/09	12/31/20			_	_	1					-		1	1	1		1 1		- 1	102,40	3	- 1	- 1	- 1	- 1	- 1	-	- 1	- 1	-	-	3	- 1	-	_	1	-	- 1	3		
		1														7				1			1														1						
EFWS (EARTHQUAKE SAFETY EMERGENCY RESPO	NSE 2014)																																										
June 2015	54,065,000	11/06/14	12/31/20																				*					-		54,0	65,000		-										
Baseline	54,347,209	11/06/14	12/31/20																		- 1				- 1			- 1		54.3	47.209		-				_	1 1					
																					1		1			1	1					- 1						1		1	1		
Current Projection	54,347,209	11/06/14	12/31/20																ļ.,					-	-	- 1	- 1	-		- 1	47,209		-	- 1	- 1			,	- 1	-	-		
		†	†		-1	-1	-1	1	11							1	1																				1	1					
EMERGENCY FIREFIGHTING WATER SYSTEM (EFV	VS) SUB-TOTAL																																										
June 2015	156,465,000																																										
Baseline	156,747,209																																										
Ourse of Brade of the s																																											
Current Projection	156,747,209																																										
