


May 13, 2024

# Capital Project Update: Castro Station Elevator

Jane Chan, Project Architect



# Castro Station Elevator

## Capital project update

Commission Approvals		
Award Date: 1/20/2023	Amount: \$11,540,000	Duration: 600 Days from NTP (6/20/2023)
Project Cost Estimate:	Amount: \$12,000,000	
Planned Modification:	Amount: N/A	Duration: 120 Days
		For a total of 780 Days from NTP to Substantial Completion including contingency
Contractor:	CLW Builders, Inc.	
Status:	Project is under construction	
Scope:	Add a new elevator and improve safety and accessibility in and around Castro Muni Station	

# Castro Station Elevator


Castro Muni Station

Market Street at Castro and 17<sup>th</sup> streets


District 8

More info:

[Castro Station Accessibility Improvements Project | SFMTA](#)

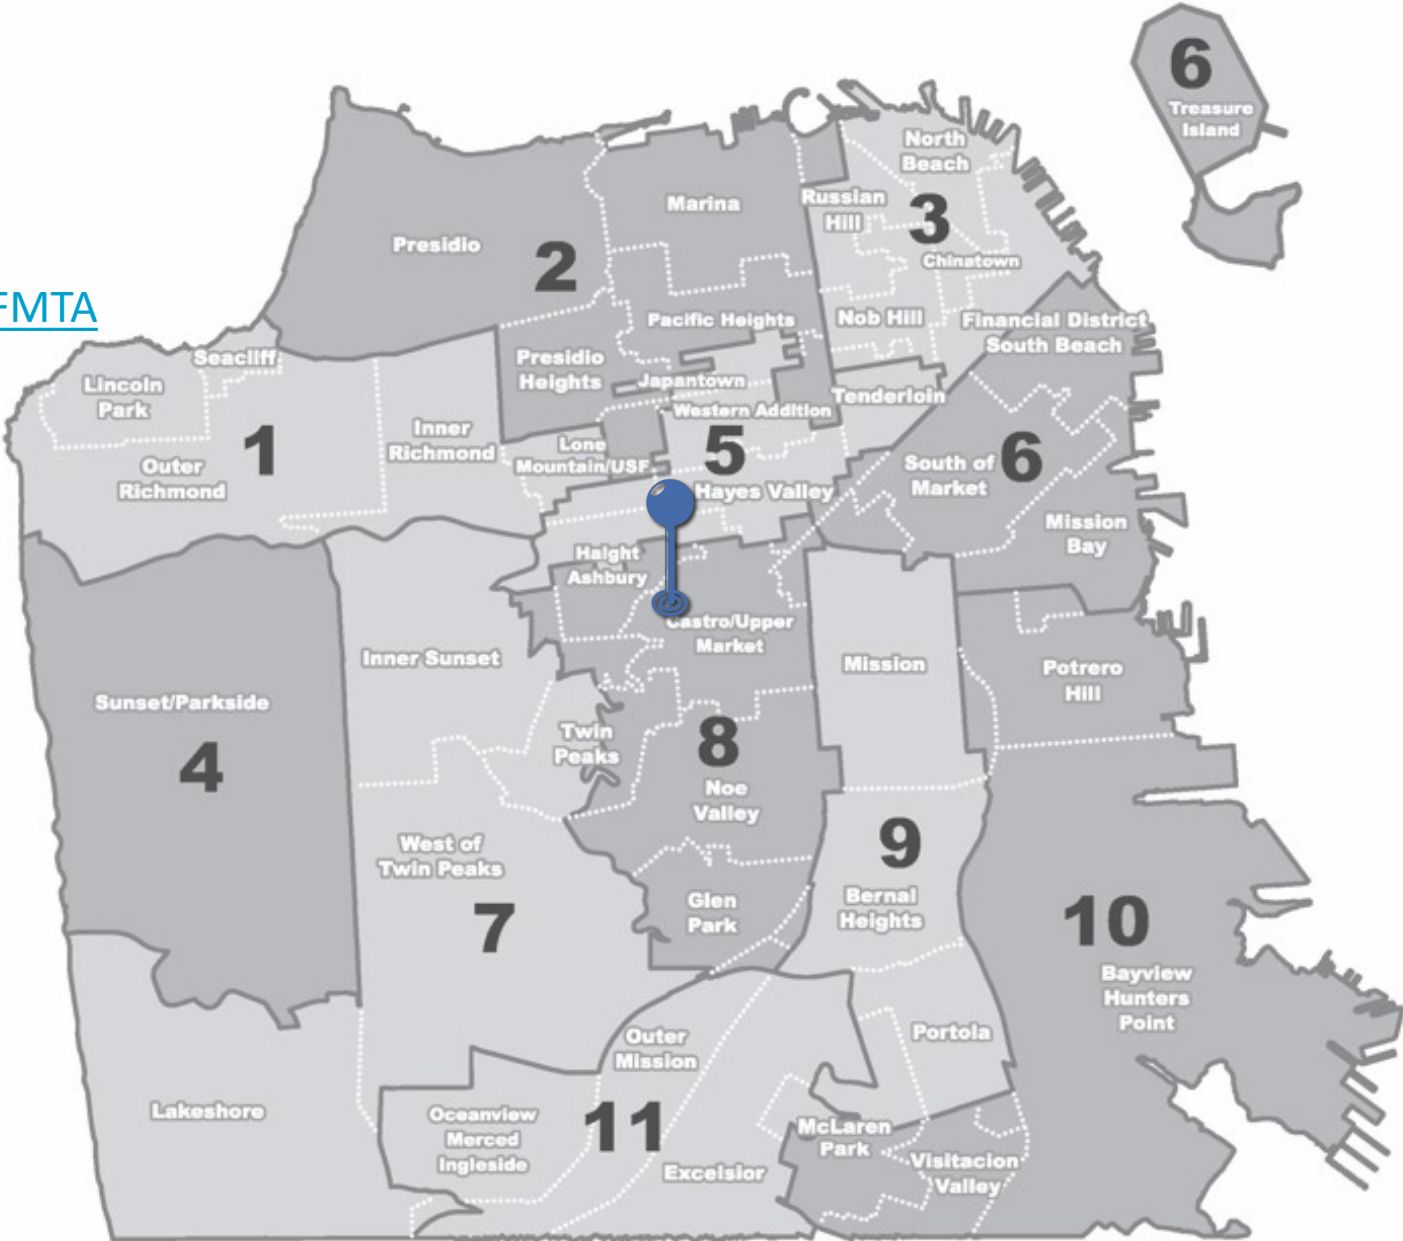

# Scope of Work – Overview

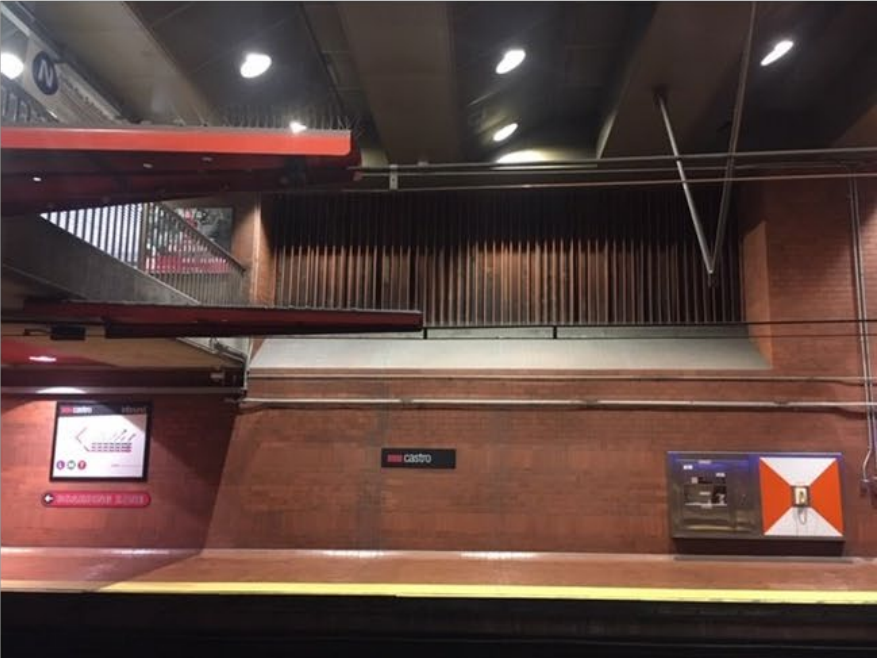

# Scope of Work – Overview

## Castro Station Accessibility Improvement Project


- Add a 4-stop elevator to access to all four levels of the Station
- Create a safe path of travel to and from the station on the southside St./Harvey Milk Plaza
- Correct cross slopes along sidewalk from Castro/Market streets to the proposed elevator entrance
- Replace dim streetlights
- Align narrow sidewalk along Market Street with existing (wider) sidewalk
- Provide new curb ramps on either sides of Collingwood and Market streets

## Novel aspects of project


- Station was completed in 1980 and is owned by BART
- Harvey Milk Plaza re-design efforts are underway



# Contract Schedule – Planned (and Modified)

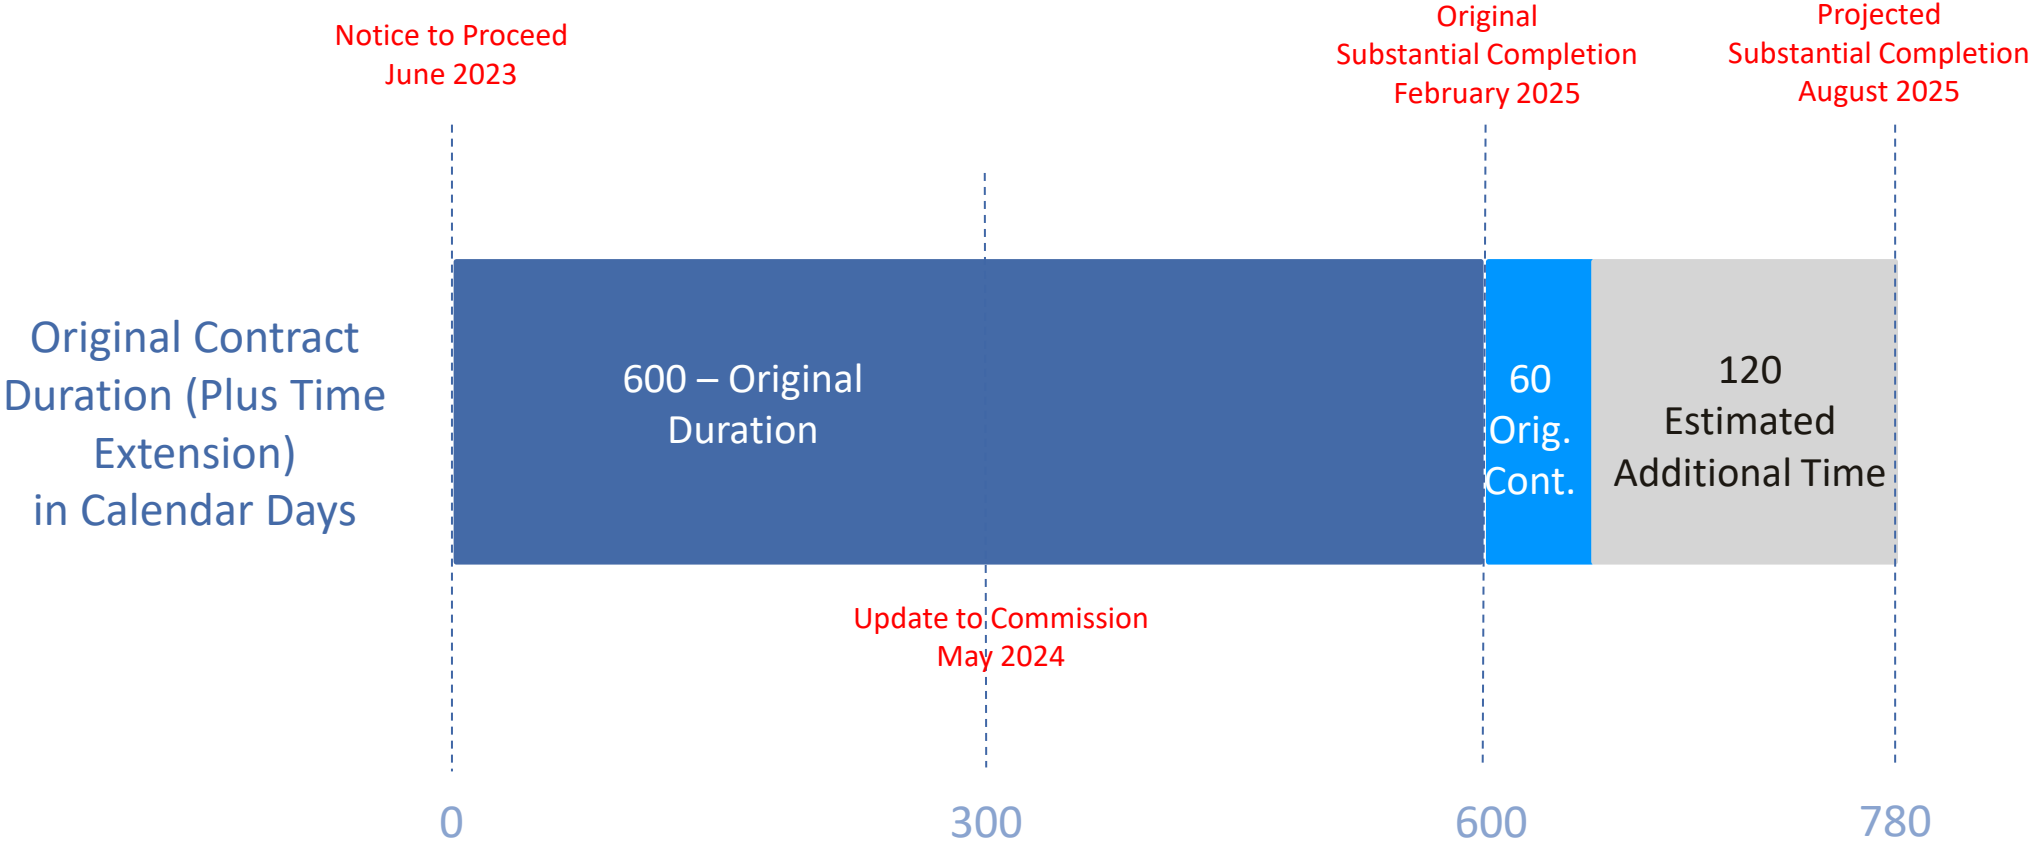

# In Progress

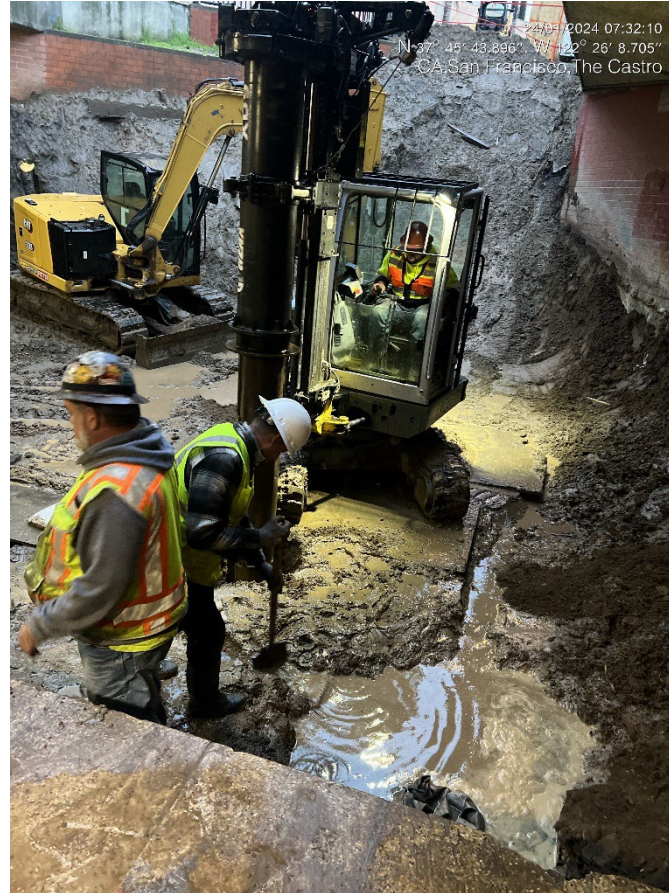

## NTP to early 2024

- BART permit
- Site preparation
- Rough grading
- Overhead lines de-energization
- Started micropile installation


# In Progress



- Micropile installation complete




# In Progress

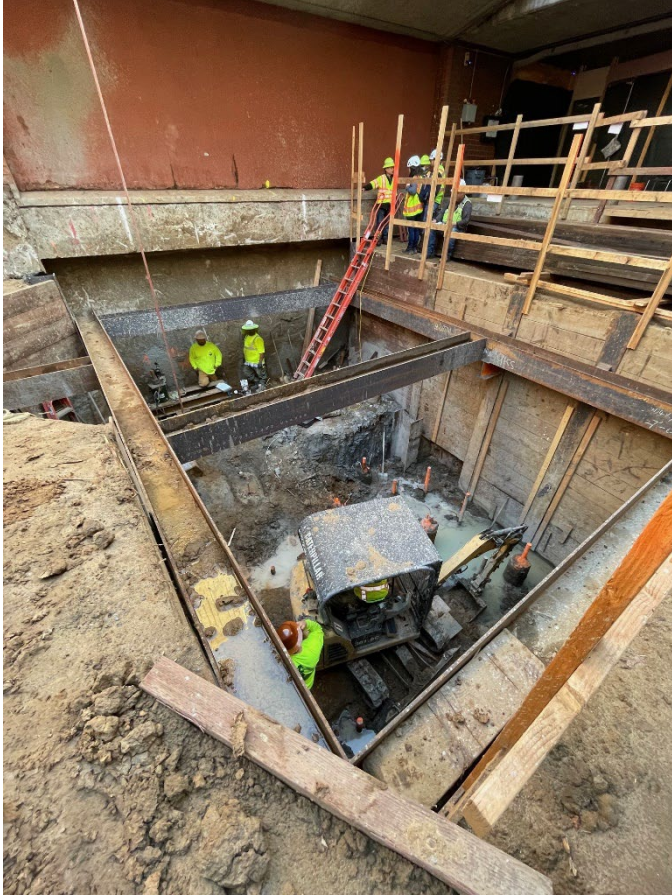

Early 2024 to now

- Micropile installation
- Underpinning
- Excavation
- Shoring and retaining wall Installation
- Foundation slab installation
- Waterproofing

# In Progress

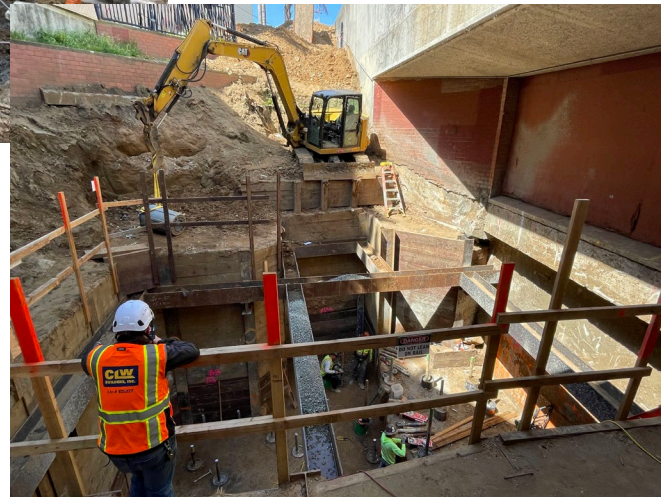

- Shoring Installation complete

# Proposed





# QUESTIONS
