
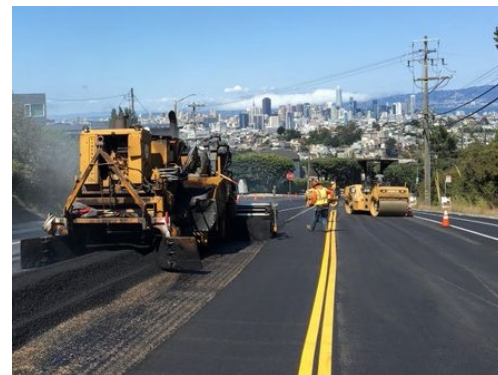
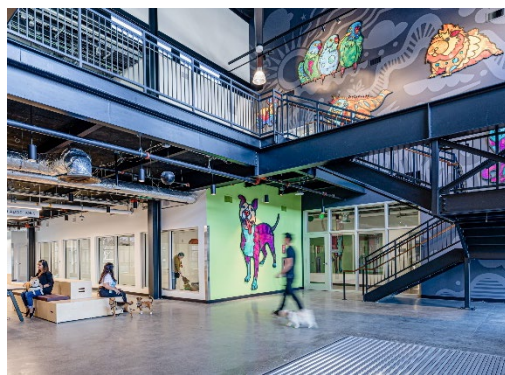


February 27, 2025

Capital Project Update: Folsom Streetscape Project

Carol Huang
Project Manager

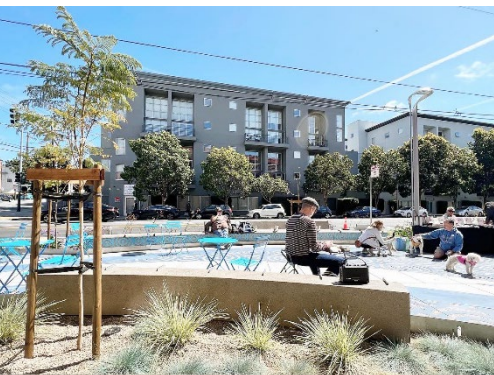

Folsom Streetscape Project

Capital Project Update

Notice to Proceed Date:
March 11, 2024

Amount:
\$34,979,747.50

Project Cost Estimate:
\$37,518,400.00

Construction Duration:
950 calendar days

Contractor:
Mitchell Engineering

Project Scope:
Complete streets improvement on Folsom Street to enhance multimodal safety

Folsom Streetscape Project Capital Project Update

Project Limit
Folsom Street
between 2nd Street & 11th Street

District 6

More info:
<https://sfpublicworks.org/FolsomSOMA>



Project Improvements Summary


- **TRANSPORTATION IMPROVEMENTS** - Two-way cycle track and new medians
- **CURB RAMP UPGRADES AND SIDEWALK WIDENING** - Widened sidewalks, bulb-outs, raised crosswalks and mid-block crossings to improve pedestrian walking safety
- **TRAFFIC SIGNAL MODIFICATION** - New traffic/pedestrian/bike signal system
- **STREETLIGHTING** - New roadway and pedestrian streetlights
- **UTILITY IMPROVEMENTS** – Wastewater/water/drainage improvements
- **TRANSIT IMPROVEMENTS** – Overhead contact system and traction power improvements, new boarding islands
- **LANDSCAPING** - New median planting and street trees
- **PAVING** – Roadway resurfacing
- **STREETSCAPE** – New placemaking improvements to include new decorative crosswalk, public benches, commemorative plaques and pole wraps

Project Improvements

Rendering for Folsom/Rausch/Hallam Streets Intersection



Project Placemaking Elements within Leather & LGBTQ District

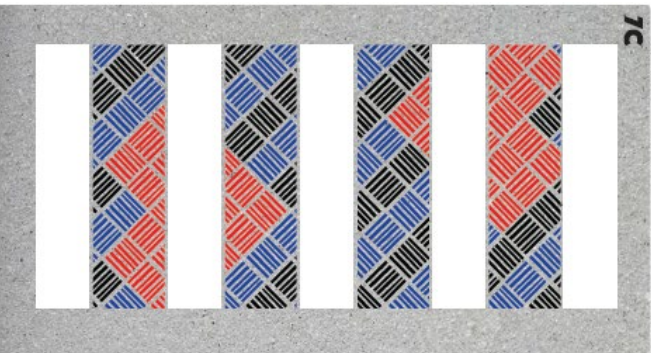

DECORATIVE CROSSWALK



COMMEMORATIVE PLAQUES



CUTURAL POLE WRAP



PUBLIC BENCH



BIKE RACK

Project Improvements


Rendering for Folsom Street and Russ Street Intersection



Rendering for Folsom Street between 5th Street and 4th Street



Project Placemaking Elements within SOMA Pilipinas District

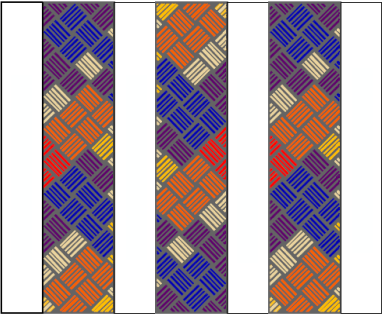

DECORATIVE CROSSWALK



PUBLIC BENCH

Project Placemaking Elements within YCBCD District



DECORATIVE CROSSWALK




YCBCD BENCH



YCBCD BIKE RACK

Contract Schedule

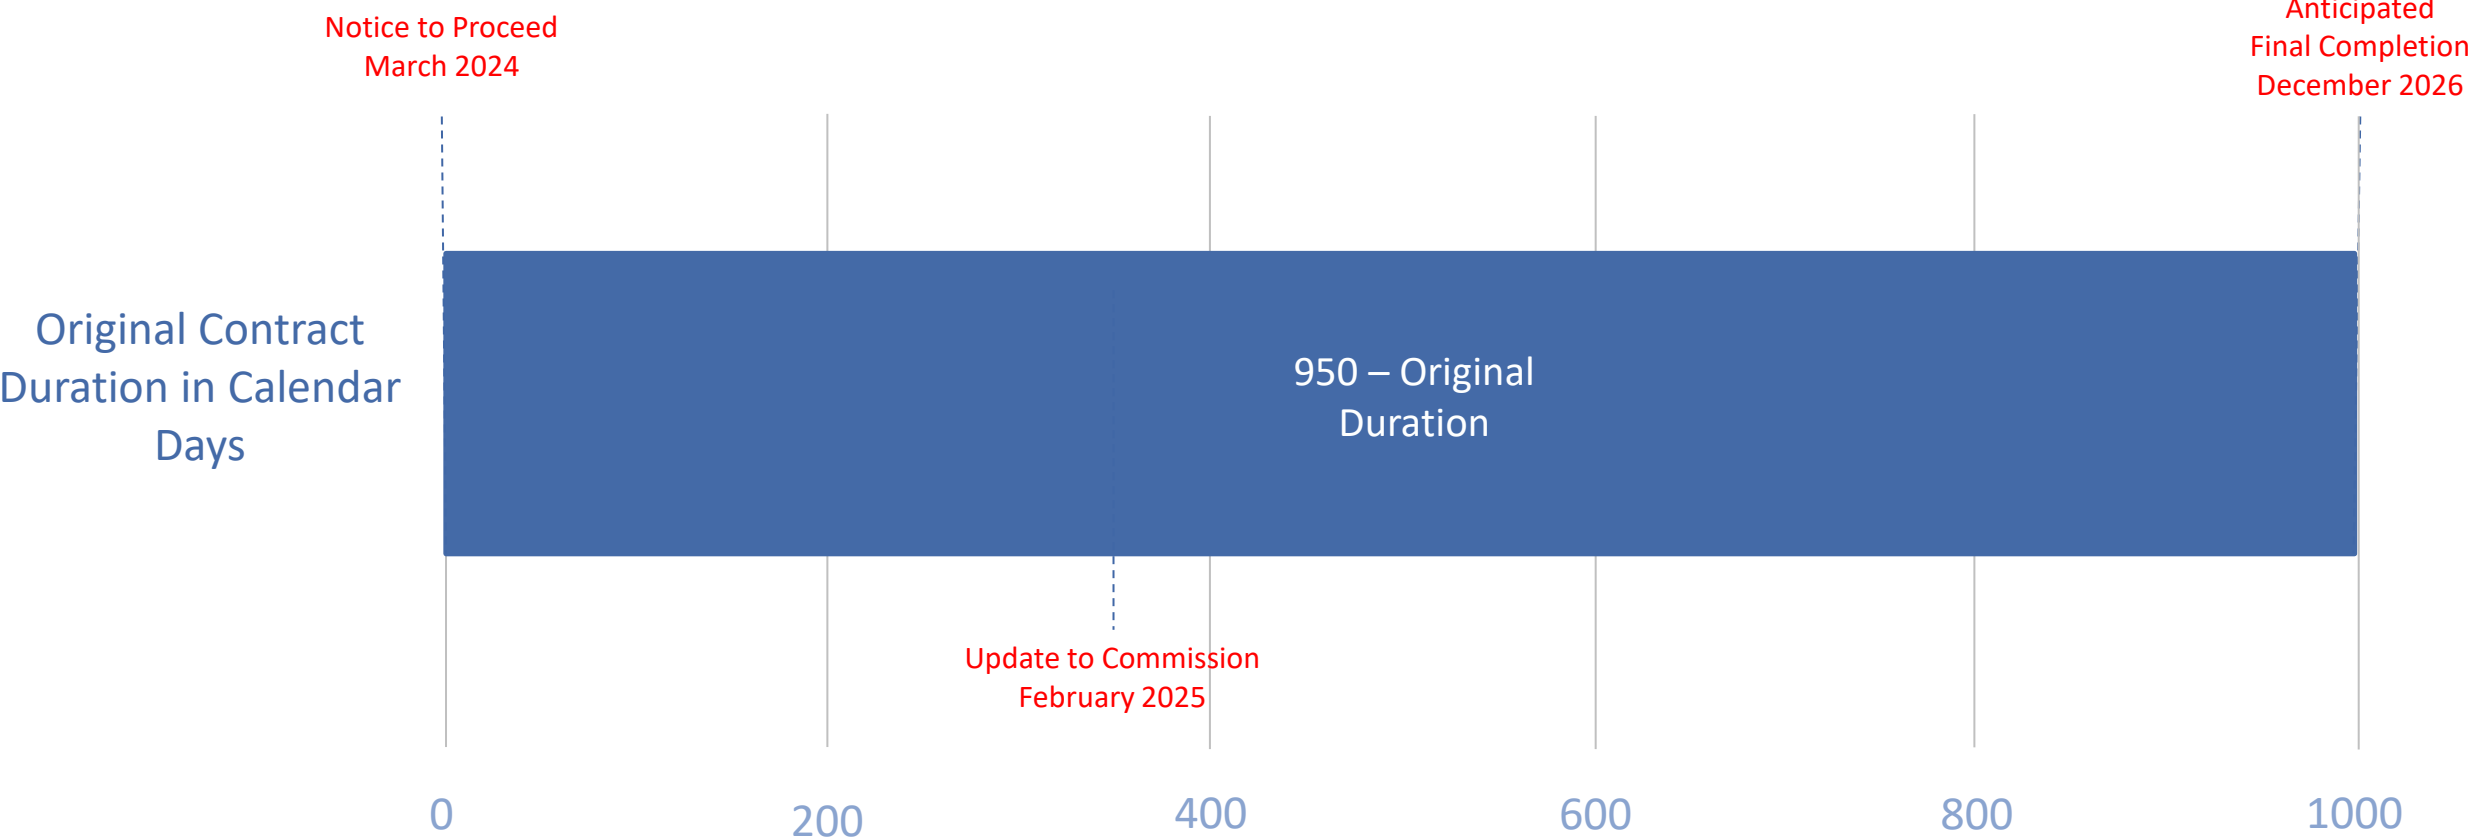

Progress Photos

Cured-In-Place Liner (CIPL) Installation between 10th – 11th St



Progress Photos (Cont.)

Main Sewer Line Upgrade & Manhole Installation Between 7th St and 8th St



Progress Photos (Cont.)

New Electrical Work – Traffic Signal & Street Lights



Progress Photos (Cont.)

PG&E and Sewer Conflict between 3rd St & 4th St



Potential Impacts to Project

- **Unforeseen Utility Conflicts ~\$1M**

Affected Scope	Unforeseen Conflicts
Sewer Replacement	Concrete encased high voltage PG&E line directly over sewer main
	Unmarked water line parallel to sewer main
	Unforeseen utilities encountered during new catch basin installations

- **Coordination with Adjacent Projects from Other Departments ~\$300K**

City Department	Project Name	Location
PUC	Folsom Area Stormwater Improvements Project	On 11 th St between Bryant and Folsom St
Rec Park	Gene Friend Rec Center Project	On Folsom St between 6 th and Harriet St

Potential Impacts to Project (Cont.)

- Major Events Coordination ~ \$75K
 - Resequencing work
 - Demobilization/Remobilization

Major Events	Impacted Project Area	Duration
Folsom Street Fair (Annual Event)	Folsom St between 8 th – 11 th St	3 calendar days
Dreamforce (Annual Event)	Folsom St between 3 rd – 6 th St	14 calendar days
NBA All Stars	Folsom St between 3 rd – 4 th St	12 calendar days
Superbowl 2026	Folsom St between 3 rd – 6 th St	18 calendar days
Various Major Conventions at Moscone Center	Folsom St between 3 rd – 6 th St	14 calendar days



Folsom Streetscape Project

Capital Project Update

Notice to Proceed Date:
March 11, 2024

Amount:
\$34,979,747.50

Project Cost Estimate:
\$37,518,400.00

Construction Duration:
950 calendar days

Contractor:
Mitchell Engineering

Project Scope:
Complete streets improvement on Folsom Street to enhance multimodal safety



QUESTIONS
