
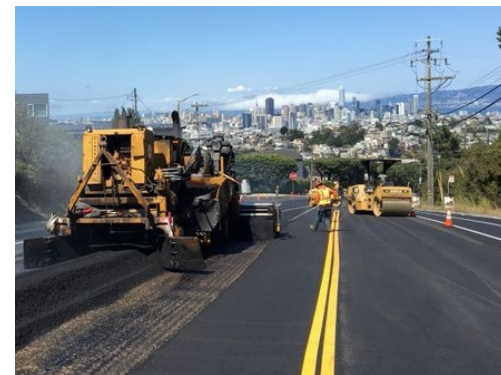
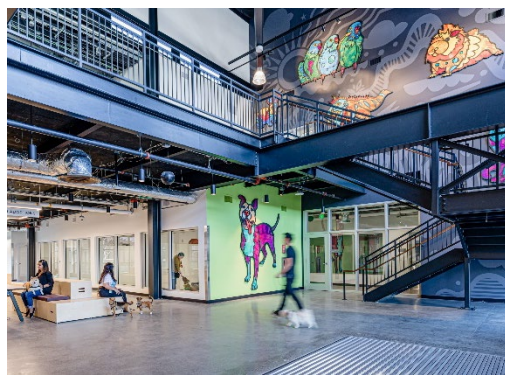


May 13, 2024

# Capital Project Update: Minnesota Streetscape Improvements Project

Trent Tieger, PE  
Project Manager

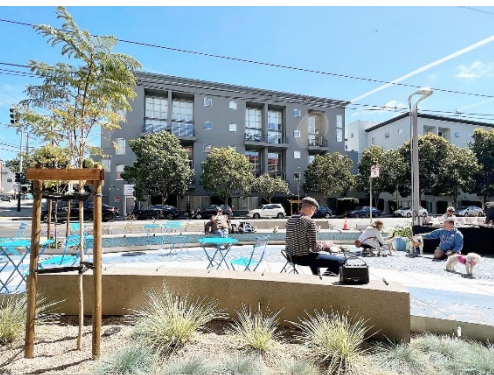

# Minnesota Streetscape Improvements Project

## Capital Project Update

Commission Approvals		
Award Date: 4/27/2023	Amount: \$2,089,297.00	Duration: 510 calendar days
Project Cost Estimate:	Amount: \$2,512,416.00	
Contractor:	Ronan Construction	
Status:	Under construction	
Scope:	Streetscape improvements on Minnesota Street, between 23rd and 25th streets, and on 23rd Street, between Minnesota and Tennessee streets. Work consists of roadway, bulb-outs, landscaping, drainage, streetlighting and all associated works	



# Minnesota Streetscape Improvements Project

## Location

Minnesota Street, 23rd Street to 25th Street  
23rd Street, Minnesota Street to Tennessee Street  
District 10

More info:  
[www.sfpublicworks.org/Minnesota-Streetscape](http://www.sfpublicworks.org/Minnesota-Streetscape)




# Scope of Work – Progress

## Planned work summary

- Streetscape upgrades along Minnesota Street from 23rd Street to 25th Street, and 23rd Street from Minnesota Street to Tennessee Street
- Constructing ADA-compliant paths and curb ramps, missing sidewalks, roadway paving, streetlighting, drainage, landscaping
- Improvements to the community-created linear greenspace, the Minnesota Grove; landscaping, ADA paths, placemaking elements



# Contract Schedule – Planned

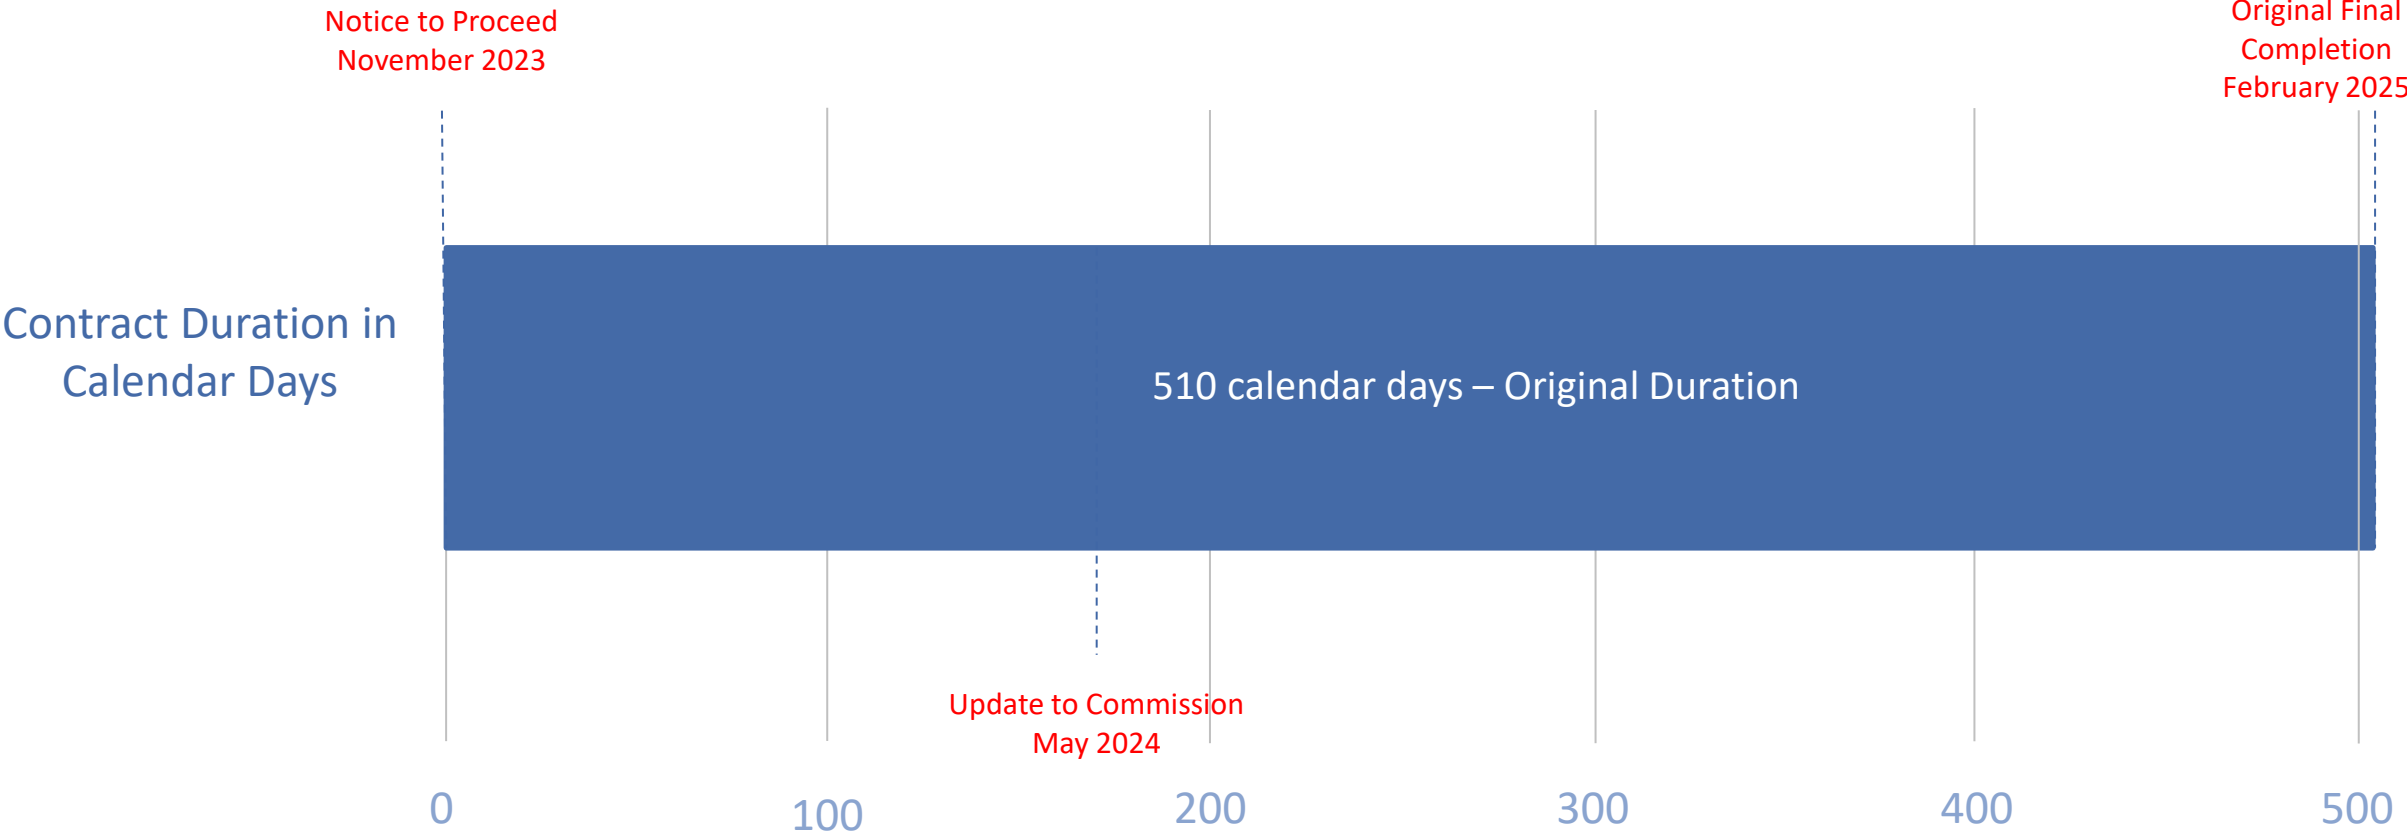

# Before and Progress



**25th & Minnesota NE Corner**  
New sidewalk, corner bulb-out, curb ramps



# Progress



## 25th & Minnesota NE Corner New sidewalk, corner bulb-out, curb ramps



# Progress



**25th & Minnesota NE Corner**  
New sidewalk, corner bulb-out, curb ramps



# Progress



## 25th & Minnesota NE Corner New sidewalk, corner bulb-out, curb ramps



# Progress



## 25th & Minnesota NE Corner New sidewalk, corner bulb-out, curb ramps



# Before and Progress



## 23rd & Minnesota New sidewalk, corner bulb-out, curb ramps



# Progress



## 23rd & Minnesota New sidewalk, corner bulb-out, curb ramps



# Before and Progress



## 23rd St, Minnesota to Tennessee New sidewalk



# Before



## Minnesota Grove

New ADA seating and path of travel, structural improvements



# Before



## Minnesota Grove

New ADA seating and path of travel, structural improvements



# Before



## Minnesota Grove

New ADA seating and path of travel, structural improvements



# Before



## Minnesota Grove

New ADA seating and path of travel, structural improvements





# QUESTIONS
