

June 10, 2024

# Capital Project Update: Mission Branch Library

Andrew Sohn  
Architect



# Mission Branch Library Renovation

## Capital Project Update


Commission Approvals		
Award Date: 12/2/2022	Amount: \$23,020,000	Duration: 730 calendar days
Contractor:	S.J. Amoroso Construction Co.	
Status:	Approximately 25% construction complete	
Scope:	Complete renovation and expansion of the Mission Branch Library	



# Mission Branch Library Renovation Location

300 Bartlett St., 94110  
District 9

More info:  
[sfpublicworks.org/missionlibrary](https://sfpublicworks.org/missionlibrary)

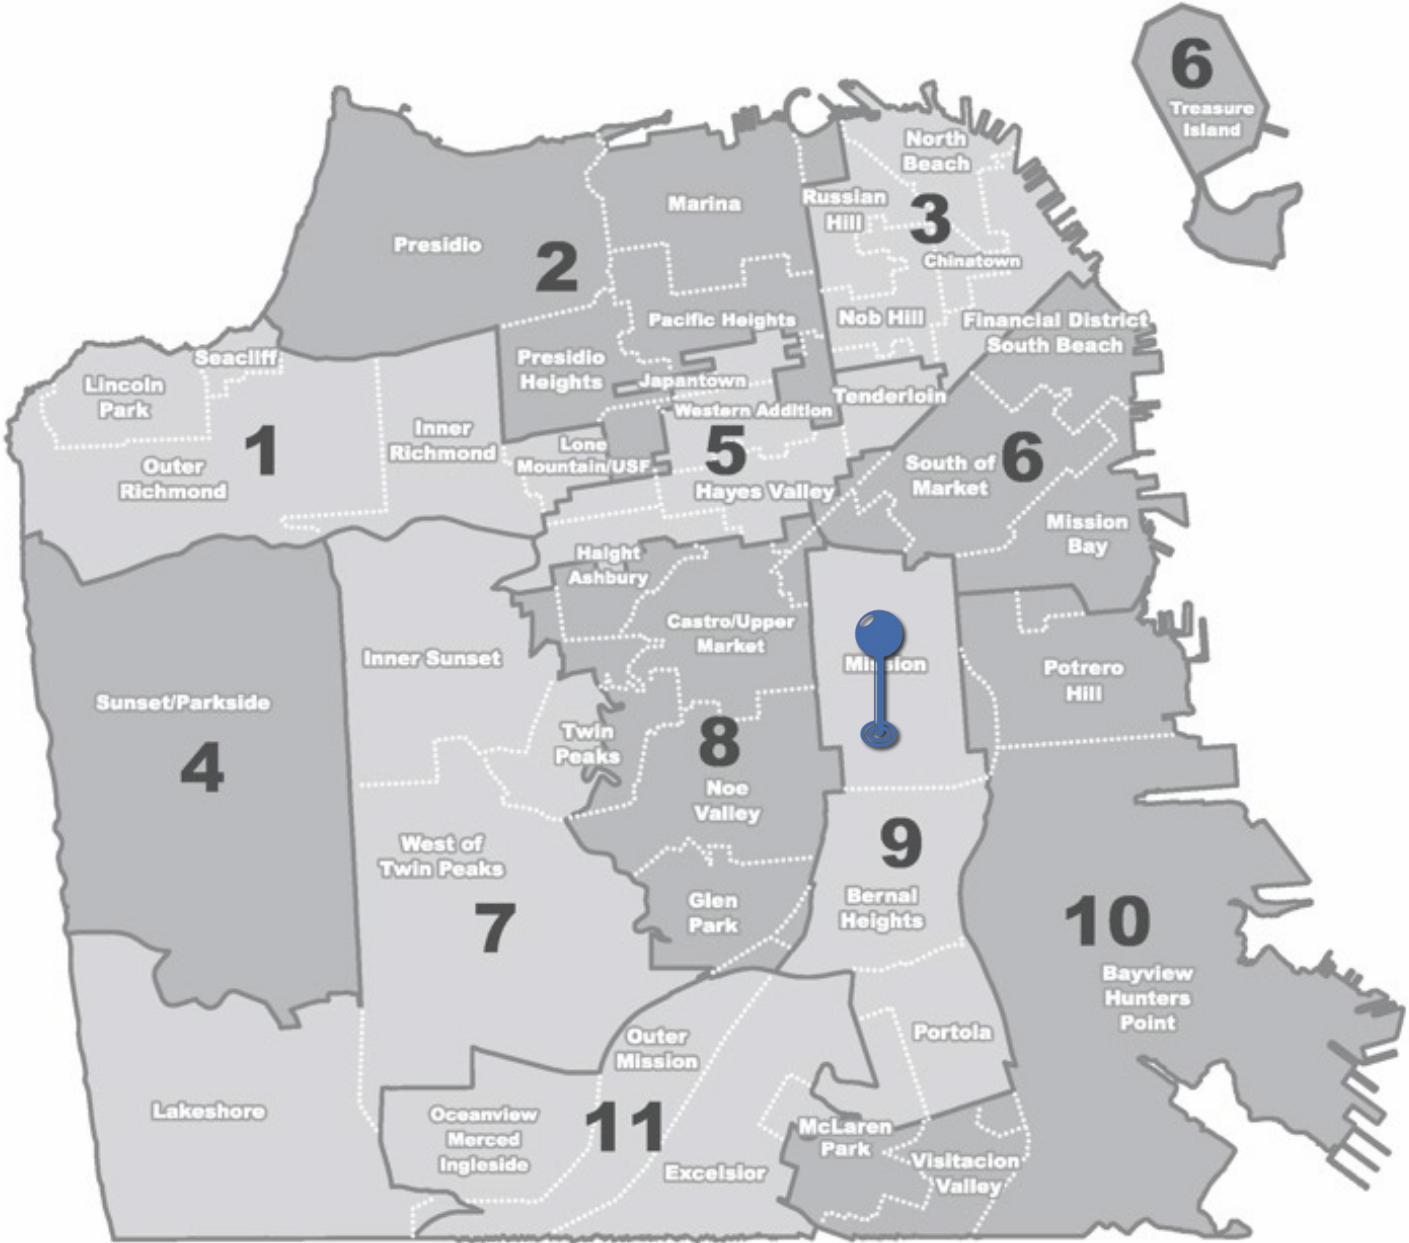

# Scope of Work - Progress


## Planned work summary:

- Complete renovation and expansion
- Replacing historic features

## Novel aspects of project:

- 1914 Carnegie library
- Small site, complex project
- Building electrification
- Partially state grant funded
- Soldier piles in lieu of underpin
- Additional vibration analysis

# Contract Schedule – Planned

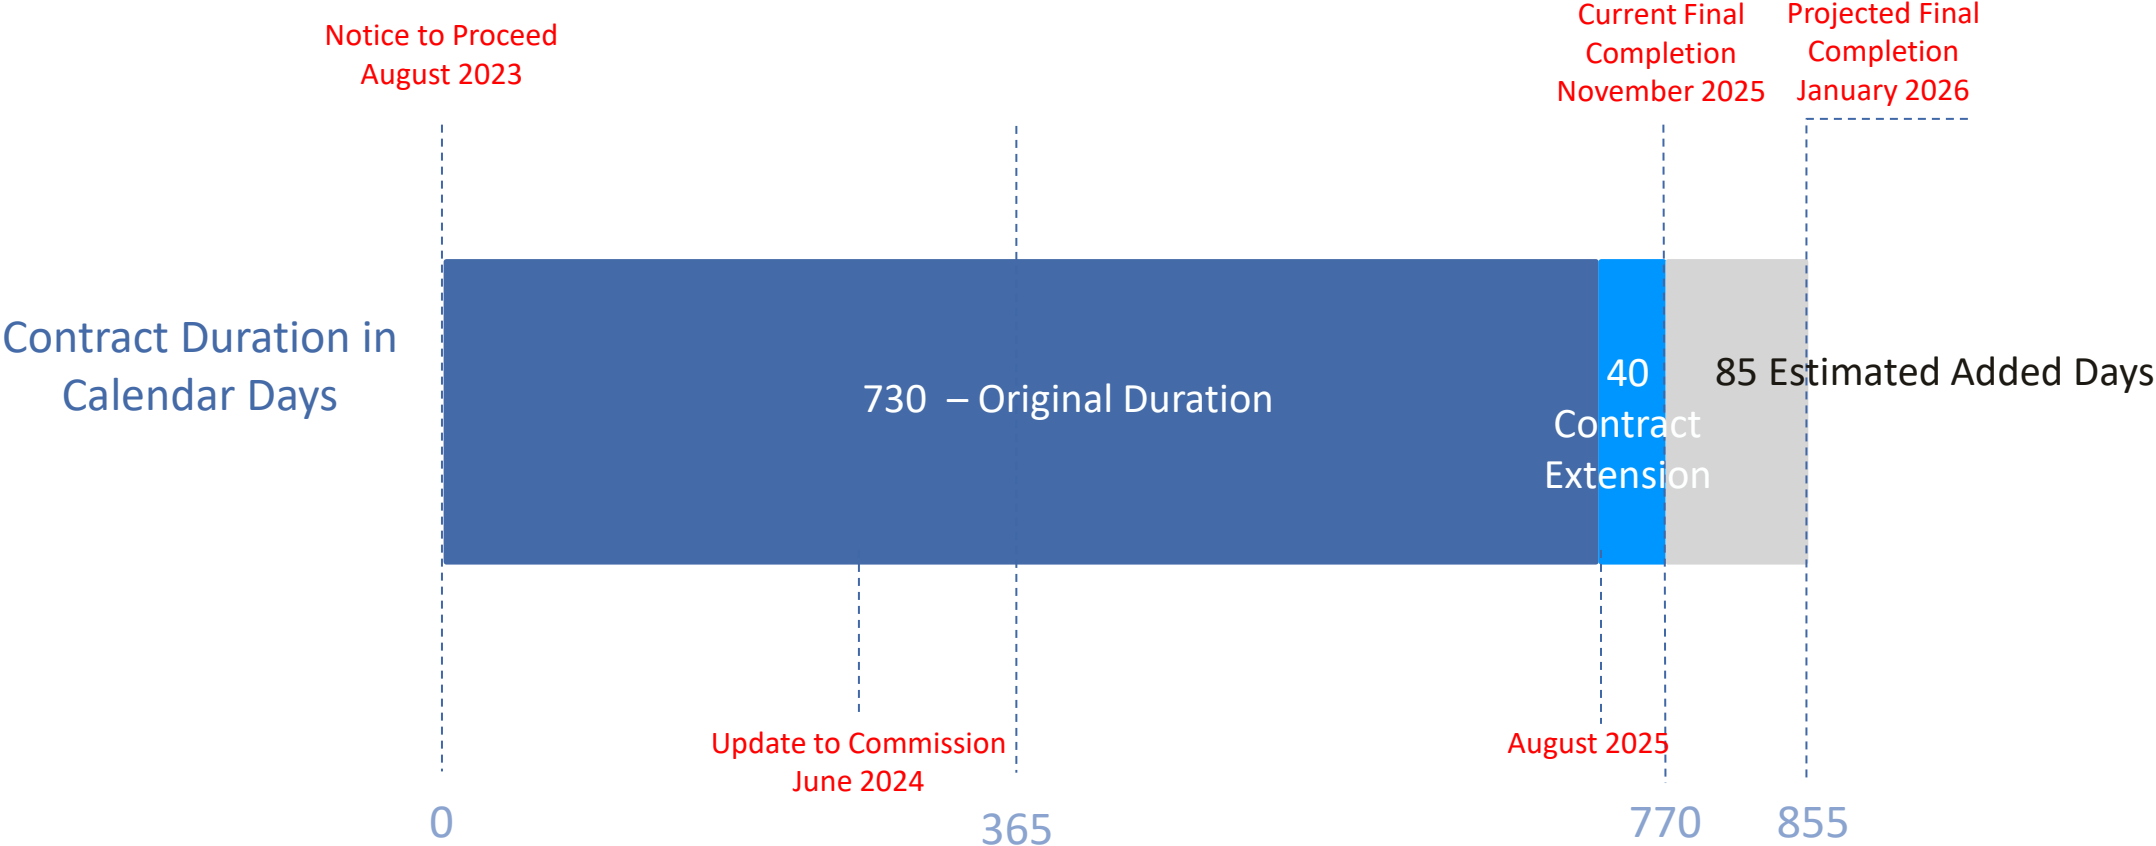

# Construction Progress



Construction kickoff, Aug. 2023



# Construction Progress



Historic reading room

# Construction Progress



Future community room



# Construction Progress



**Demolition of courtyard and  
PG&E equipment**



# Construction Progress



Interior construction



# Construction Progress



**New foundations and building underpinning**



# Construction Progress



Installing shoring piles

# Design Images



Final design sketches



# QUESTIONS
